


# WELCOME TO THE SOUTH CENTRAL DISTRICT Transportation Board Presentation



Presentation by Rod Lane, P.E.  
South Central District Engineer  
January 19, 2018

# Southcentral District Boundaries

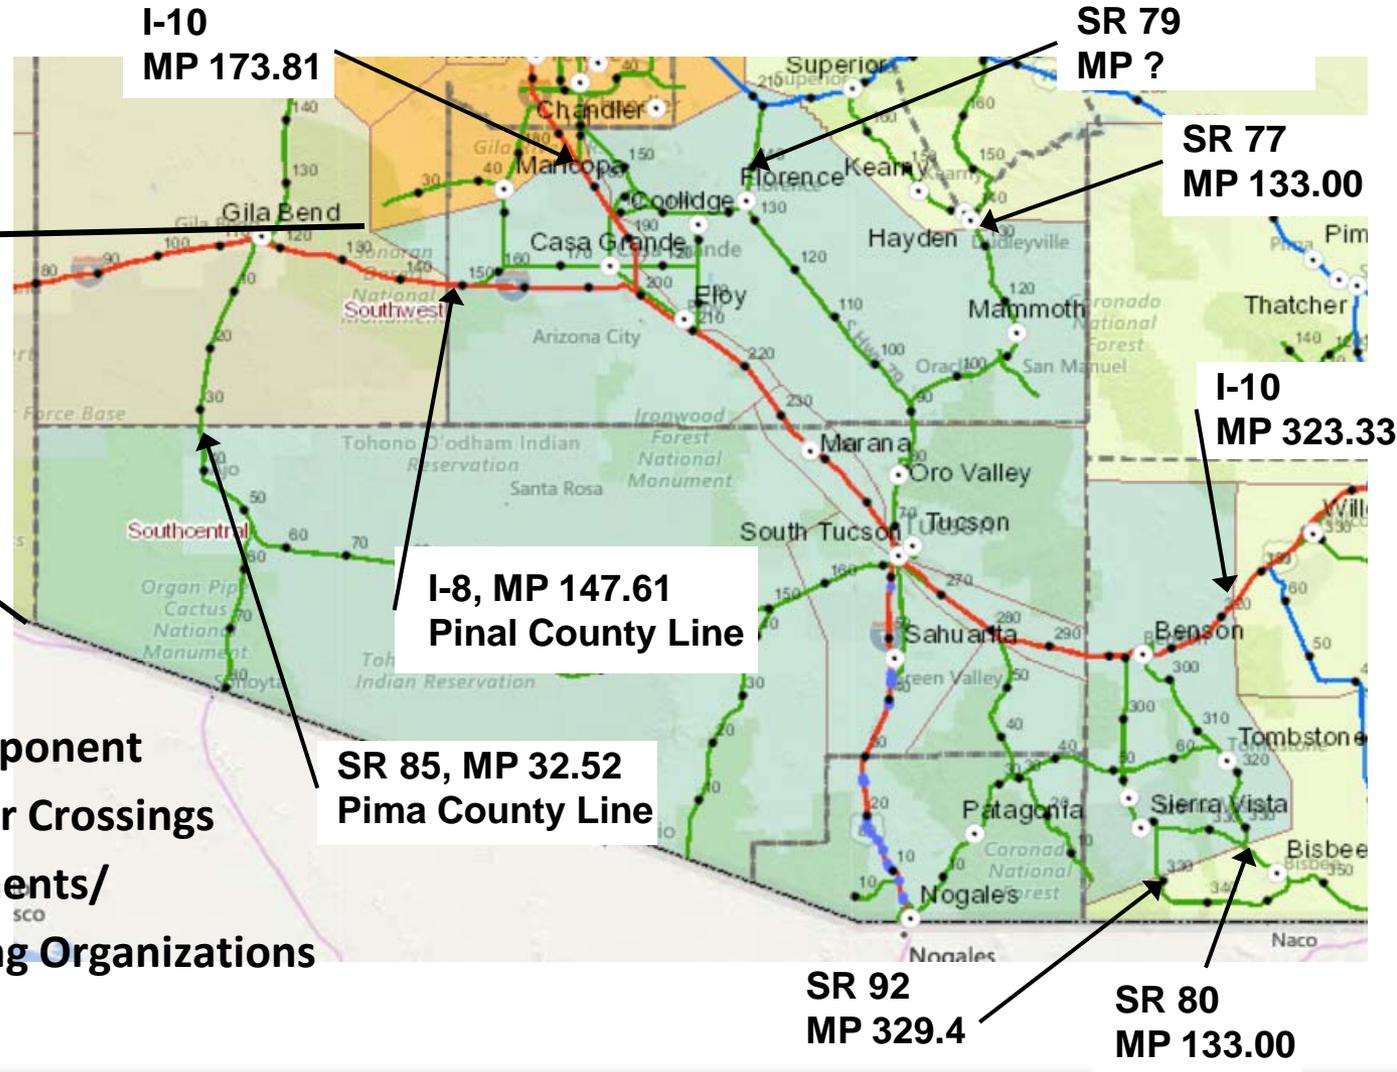


- ▶ **3 Interstates**
- ▶ **Significant Rural Component**
- ▶ **4 International Border Crossings**
- ▶ **5 Council of Governments/  
Metropolitan Planning Organizations**
- ▶ **5 Tribal Nations**

# SR90 @ MP 316

- ▶ Scope:  
Intersection Reconstruction
- ▶ Contractor: KE&G
- ▶ Contract Value: \$2.63M
- ▶ 30% Complete
- ▶ Expected Completion: Aug 2018



# SR90 @ MP 316

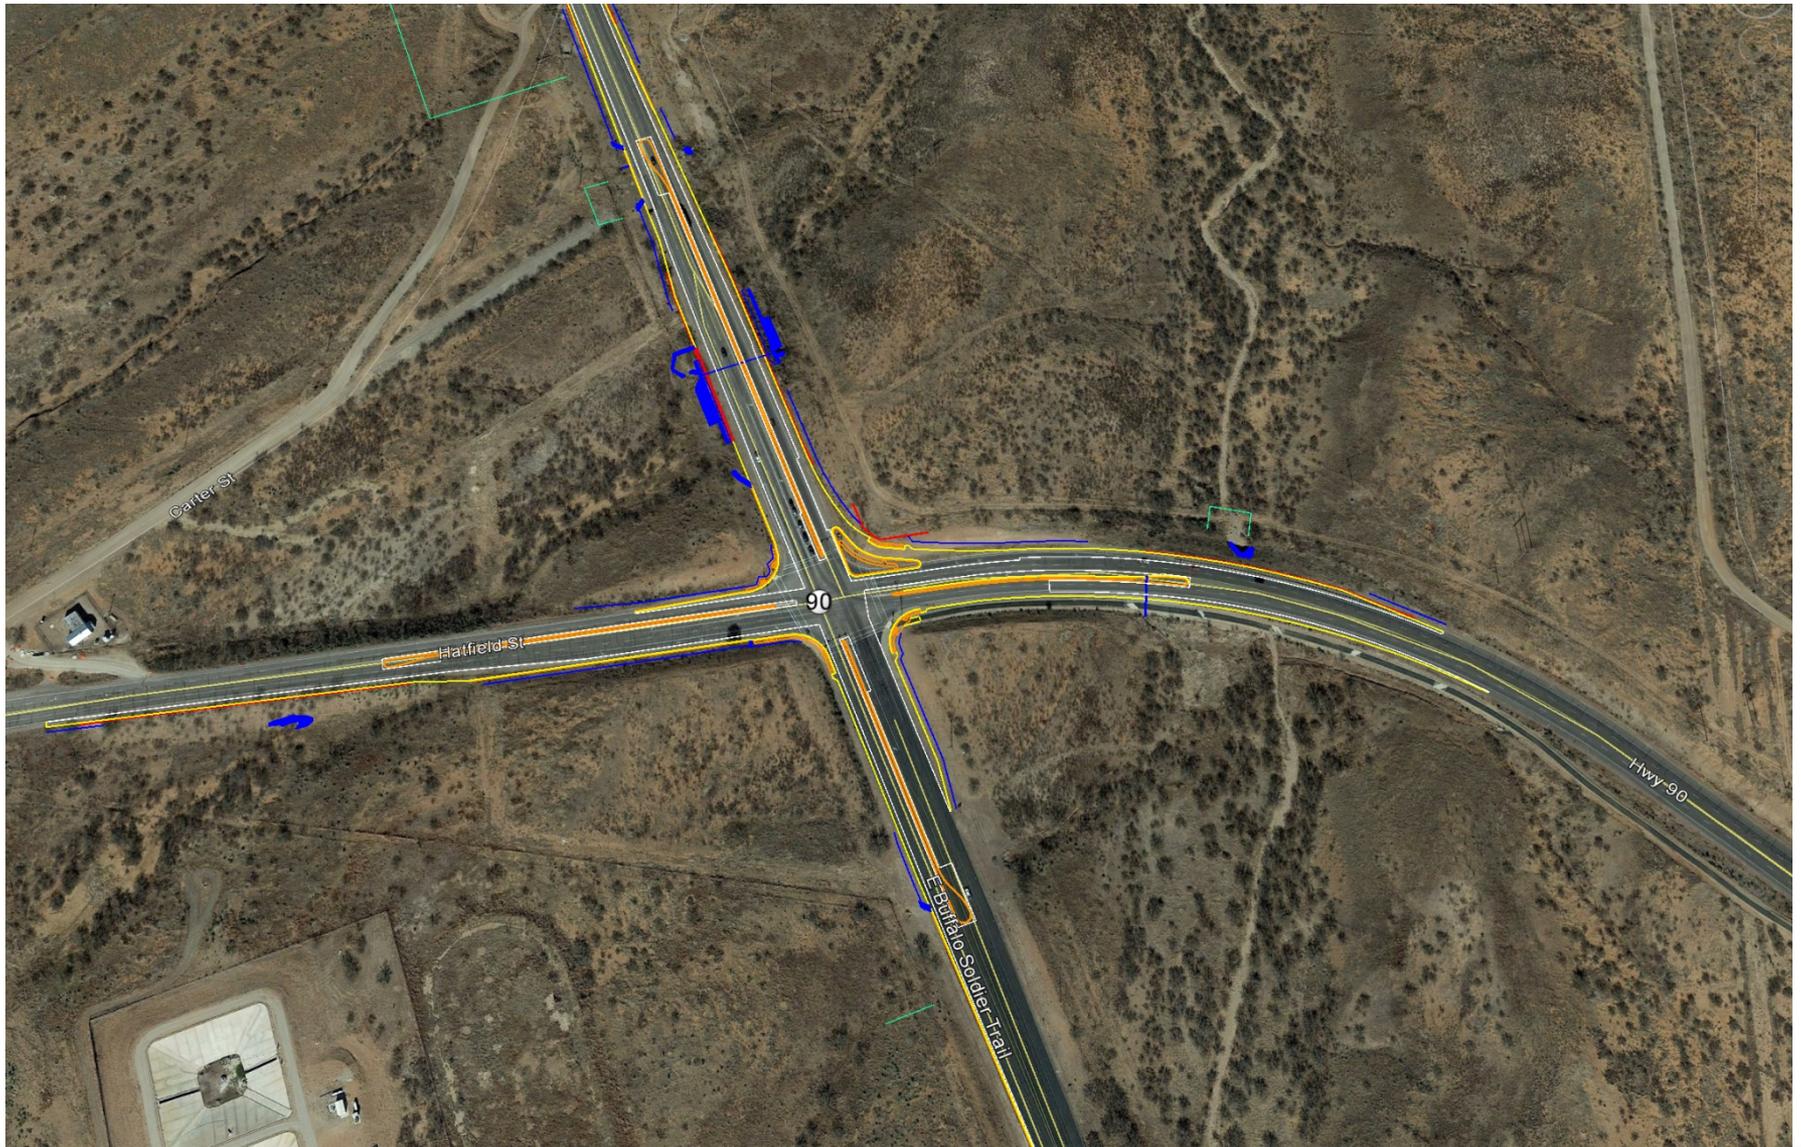

# SR92 @ MP 321.21 (Fry's Blvd) to MP 325.25 (Kachina)



- ▶ Scope:
  - Mill and fill SR 90 to Kachina
  - Reconstruct South of Busby Dr. to South of Foothills Dr.
- ▶ Currently Advertised
- ▶ Programmed Amount \$9.5M
- ▶ Bid opening Feb 9<sup>th</sup>
- ▶ Est. start Mid April 2018
- ▶ Est. completion: Dec 2018

# SR77 Tiger Mine to Miguel

- ▶ Scope:
  - 6.8 Miles of Mill and Fill and Deck resurfacing from Miguel to Old Tiger Rd
- ▶ Contractor: FNF
- ▶ Contract Value: \$4.32M
- ▶ 40% Complete
- ▶ Expected Completion: April 2018




# Ina Road Traffic Interchange

- ▶ Contractor: Sundt/Kiewit Joint Venture
- ▶ Contract Value: \$124M
- ▶ 50% Complete
- ▶ Expected Completion: 1/2019



# I-19 Ajo TI

- ▶ Reconstruct Traffic Interchange to Single Point Urban Interchange
  - Ongoing Activities: Retaining Walls; WB Ajo bridge, and RCBC
- ▶ Contractor: Ames Construction Inc.
- ▶ Contract Amount: \$39.9M
- ▶ 95% complete
- ▶ Expected Completion: 3/2018

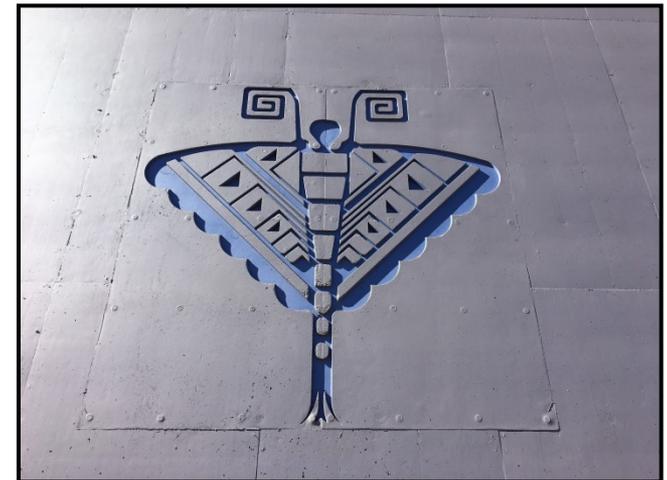

# SR 86 Kinney to Valencia

- ▶ Roadway widening, Drainage and Safety Improvements
  - Ongoing Activities: Earthwork, paving, RCBC and traffic signals
- ▶ Contractor: The Ashton Company
- ▶ Contract Amount: \$40.9M
- ▶ Expected Completion: Fall 2018



# I-10 over Wilmot

- Scope:
  - Superstructure replacement
- Contractor: Pulice Construction
- Contract Value: \$3.9M
- Superstructure rehabilitation using a temporary bridge.



# I-10/SR87 in Picacho

- Contractor: Coffman Specialties
- Contract Value: \$58.5M
- Mainline Widening and New T.I.
- New Dust Detection and warning system



# I-10:

# I-8 to Early Rd

Apparent Low Bidder:  
Ames/Combs JV



# Current Construction

Project Name	Contractor	Location Route and Mile Post	Quick Status	Contract Time			Project Dollars			Up-Coming Activities (paving, bridge forming, sign installation, other)	Estimated Completion (year/month)
				Contract Time Days	Time Used Days	% Complete	Contract \$	\$ Spent	% Spent		
H847901C - INA ROAD TI	SKJV	I-10, MP 248	-0.02	885	361	41%	\$85,628,517	\$33,174,215	39%	UPRR BRIDGE GIRDERS, DEMO OLD WB I-10 MAINLINE AND BRIDGE	2019/JUNE
SB413 - INA ROAD, SILVERBELL TO STARCOMMERCE	SKJV	INA ROAD, MARANA	0.02	885	361	41%	\$22,504,912	\$8,722,992	39%	DEMO OLD INA ROAD BRIDGE, CURB, GUTTER, SIDEWALK, PAVING	2019/JUNE
CANOA RANCH TO DUVAL H871601C	Ashton	I19, 31.8-42.5	0.21	420	87	21%	\$9,477,799	\$0	0%	BRIDGE BARRIER REPLACEMENT, BRIDGE DECK JOINTS	2018/DEC
H846701C SR 86 AND I-19 TI	Ames	SR 86 AND I-19	0.04	700	701	100%	\$39,973,370	\$38,571,222	96%	WORKING ON BRIDGEDECK POUR SPUI BRIDGE DECK 12/15/17, SIGNS AND ELECTRICAL, AND SEEDING	2018/JAN
H817801C, PIMA MINE ROAD TI	KE&G	I-19 AND PIMA MINE ROAD	0.14	385	294	76%	\$4,748,522	\$2,940,863	62%	FORM NB I-19 BRIDGE DECK AND PLACE REBAR	2018/APRIL
SZ13001C, CITY OF COOLIDGE	Nesbitt	MAIN ST, COOLIDGE AV-PINKLY	0.02	170	102	60%	\$1,794,540	\$1,036,186	58%	SWITCHED TRAFFIC ONTO PHASE I AND BEGAN WORK ON PHASE II THE SECOND HALF OF MAIN STREET	2018/APRIL
H879101C, TUCSON-ORCLE-GLOBE HWY	FNF	OLD TIGER RD-MIGUEL RD	0.06	120	51	43%	\$4,319,274	\$1,569,748	36%	WORKING ON THE TEMPORARY DETOUR, CONCRTE ADA RAMS, DRIVEWAYS, AND SIDEWALK	2018/APRIL
F006301C, TUCSON - BENSON HWY I-10	Pulice	WILMOT TI OP AND EARP WASH	0.05	380	45	12%	\$3,979,255	\$272,877	7%	SHORING, STRUCTURALX, AC SHOULDER REMOVAL	2018/DEC
F002301C, BENSON - STEINS PASS HWY I-10	FNF	DRAGOON ROAD TO JOHNSON ROAD	0.01	230	45	20%	\$1,635,585	\$329,221	20%	SETTING UP BARRIER	2018/JUL
H790401C, ORACLE JCT-FLORENCE SR79	Combs	SR 79, MP 132.13	0.01	160	136	85%	\$618,962	\$534,035	86%	REPLACE A SIGN, PUNCH LIST	2018/JAN
H821301C, Rest Areas	Ashton	I-10, I-91	0.01	360	5	1%	\$4,355,955	\$1,640	0%	STOPPING TIME TILL JANUARY 8, 2018	2018/DEC
H879001C, SR 84	Grey Mountain	BURRIS TO FIVE POINT	0.49	230	80	35%	\$1,747,683	\$1,465,412	84%	WORK IN RAIL ROAD RIGHT OF WAY	2018/JUNE
SZ03501C, CITY OF NOGALES	KE&G	CRAWFORD STREET	0.22	130	108	83%	\$447,500	\$468,979	105%	PUNCH LIST SUBSTANTIAL COMPLETION	2018/JAN
F000201C, NOGALES - TOMBSTONE HWY SR 82	KE&G	RIAN VALLEY WASH STR # 395	0.05	90	29	32%	\$527,974	\$194,167	37%	SHOTCRETE	2018/FEB
H880301C - E. BUFFALO SOLDIER TRAIL - HATFIELD ST	KE&G	SR 90 / MP 316	0.02	300	88	29%	\$2,633,000	\$830,149	32%	ROADWAY WIDENING, MEDIAN CONSTRUCTION, SIGNAGE, STRIPING	2018/AUG
H680601C - VALENCIA RD - KINNEY RD (SR 86)	Ashton	SR 86 / MP 159.0-166.6	0.08	700	684	98%	\$40,960,323	\$36,673,050	90%	ROADWAY, BANK PROTECTIONS, SEWER, ELECTRICAL, SIDESTREETS, SIGNAGE, STRIPING	2018/AUG

# ADOT 5-Year Program



# Interstate 10

PAG	FY 18	I-10: TI (Wilmot, Kolb and Rita)	Traffic Signalization	\$ 2 M
PAG	FY 18	I-10: Eastbound Off-ramp at SR 83	Intersection Improvement	\$ 200 K
	FY 19	I-10: Ruthrauff Rd TI	Interchange Reconstruction	\$ 104 M
	FY 19	I-10: Wash Bridge #463 @ MP 277	Scour Retrofit	\$ 150 K
PAG	FY 19	I-10: Vail Rd TIUP & Mtn View TIUP	Bridge Deck Rehab	\$ 4 M
	FY 20	I-10: SR 587 to SR 387	Pavement Preservation	\$ 23 M
PAG	FY 20	I-10: Pinal Air Park TI	Bridge Deck Replacement	\$ 2 M
	FY 20	I-10: Houghton Road TI	Interchange Reconstruction	\$ 40 M
PAG	FY 21	I-10: Ina to Ruthrauff	Mainline widening	\$ 144 M
PAG	FY 21	I-10B: Benson Bypass	Pavement Preservation	\$ 9.8 M

# Interstate 8 and 19

PAG	FY 18	I-19: Ajo Way TI (Phase 2)	Roadway Capacity	\$ 30 M
	FY 19	I-8: SW Maricopa to S of Stanfield	Pavement Preservation	\$ 22 M
PAG	FY 20	I-19: Duval Mine Rd TI - Pima Mine Rd TI	Pavement Preservation	\$ 16.3 M
	FY 20	I-19: Ruby Rd TI	Bridge Deck Rehab	\$ 2 M
	FY 20	I-19: El Toro Rd	Bridge Deck Rehab	\$ 5 M
	FY 20	I-19: Helmet Rd TI	Bridge Deck Rehab	\$ 2 M
	FY 21	I-19: Tubac to Arivaca Rd	Pavement Preservation	\$ 29 M
	FY 21	I-19B: Potero Canyon Bridge	Scour Retrofit	\$ 350 K

# Pima County

PAG	<b>FY 18</b>	SR 86: MP 82 - 102	Fence Replacement	\$ 1.6 M
PAG	<b>FY 19</b>	SR 86: Fresnal to MP 123.6	Shoulder Widening	\$ 10 M
PAG	<b>COMBINED</b>	<b>FY 20</b> SR 77: River Rd to Magee	Pedestrian Sidewalks	\$ 12 M
PAG		<b>FY 20</b> SR 77: River Rd to Magee	Street Lighting	\$ 2.5 M
PAG		<b>FY 20</b> SR 77: Orange Grove	Intersection Improvements	\$ 100 K
PAG		<b>FY 20</b> SR 77: River Rd – Calle Concordia	Pavement Preservation	\$ 11 M
PAG		<b>FY 20</b> SR 86: MP 88.25 - 90.4	Guardrail Replacement	\$ 302 K

# Pinal County

<b>FY 18</b>	SR 79: Gila River Bridge (D/18, C/20)	Bridge Deck Rehab	\$ 2 M
<b>FY 18</b>	SR 87 @ Ruins Drive	Traffic Signalization	\$ 87 K
<b>FY 19</b>	SR 77: Power Line to San Manuel Road	Safety Improvement	\$ 1 M
<b>FY 19</b>	SR 87: Wash Bridge #355, MP 117	Scour Retrofit	150 K

# Santa Cruz County

<b>FY 19</b>	SR 189: Mexico Border to Grand Ave	Construction	\$ 65 M
<b>FY 20</b>	SR 82: Sonoita Creek Bridge	Scour Retrofit	\$ 240 K
<b>FY 20</b>	SR 82: Casa Blanca Wash Bridge	Scour Retrofit	\$ 180 K

**THANK YOU**  
rlane@azdot.gov



**BE SAFE**
